



September - October 2022

Pōrangahau Road Water Supply Upgrade

Kia ora,

Welcome to another monthly update - where we will update you on what's been happening on your street throughout September and October.

What's been happening in over the last month?

As we continue to battle this terrible weather, we are pleased to let you know that we are still making good progress on this project. Over the last month the following has been completed:

- Completed directional drilling and pipe installation for stage one. (Lake View Road to Peterson Place). You may have seen the team along with various plant pulling the pipe through the ground.
- Backfilled most of the open trenches that were in place for directional drilling.
- 10 connections, 63 rider mains and two of three hydrants have been installed throughout stage 1.
- Traffic management remains in place, and you will notice that this will continually change as needed. This to open up the road where possible whilst still protect the contractors working on site as well anyone using the road (pedestrians, cyclists, and vehicles).
- Preconstruction pipe welding and site exploration is underway for Stage two (Peterson Place to Gaisford Tce).



Figure 1: Pipe being pulled through.

Figure 2: Pipe welding underway in the Fulton Hogan container.

#the BIG Water Story



What's happening during October - November?

- Site exploration will continue for Stage Two of the project (Peterson Place to Gaisford Terrace). This is to allow an understanding of what lies beneath in order to not disturb the current water network.
- Lateral connection will continue for stage one.
- Preconstruction pipe welding and site exploration will continue for Stage two.
- Directional drilling for stage 2 will begin, along with rider main and hydrant installation.

FAQ's

When will the project start and how long will it take?

The project will start in July 2022 and be completed by May 2023. We will update this information as the project progresses through flyers and on our website.

Will the area be left safe and tidy over the weekends and outside of work hours?

Yes, contractors will ensure all areas are left safe and tidy, with barriers around any excavations and residents informed of potential risks outside of working hours.

Will there be disruption to my water supply?

There will be minor disruptions while the water supply is changed over from the old supply to the new supply. We will communicate with affected residents in advance of any water supply shutdowns. If you are reliant on water, please do advise your key council contact. We expect to replace 22 laterals between Lake View Rd and Peterson Place, and 34 between Peterson Pl and Gaisford Terrace.

Will there be any traffic interruptions or diversions?

There will be traffic management in place to ensure the safety of residents and teams undertaking the work. We will work with Fulton Hogan to ensure residents are aware of the project and to keep these traffic interruptions to a minimum.

Will residents have any restrictions to access their homes?

There won't be any major restrictions, although there may be short periods of time when access to some driveways is limited. Individual property owners/tenants will be advised in advance.

Will there be a lot of noise?

There will be some noise because of vehicle movements and equipment operation. The impact of noise on the community will vary according to the time of day, nature of work and proximity to the noise source.

What are the hours of work on site?

The Fulton Hogan team are permitted to work on site from 7.00am to 6.00pm Monday to Saturday. No work, other than emergency or maintenance work, will be undertaken on Sundays and Public Holidays without prior approval by Georgia Stone, Project Manager.

#the BIG Water Story



More information

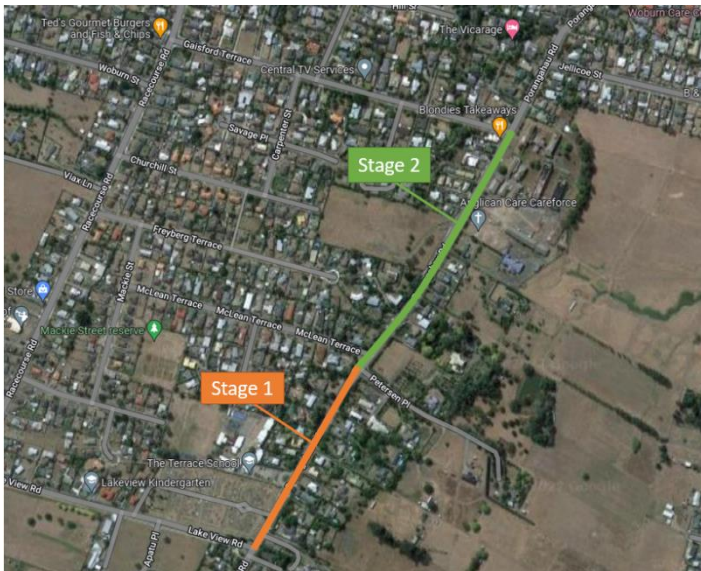


Figure 3: Stages outlined



For more information, head to our website by scanning the QR code, or get in touch with your key council contact,

- Georgia Stone (Project Manager) on 06 857 8060 or georgia.stone@chbdc.govt.nz or;
- Stephen Barns (Fulton Hogan) on 027 281 8714 or Stephen.Barns@fultonhogan.com
