

# Updates

## Programme Overview

May and June 2019, has seen the physical commencement of two further projects, we continue to progress a number of projects from tender to commencement. We expect the next two-three months will continue this trend and up to nine Big Water Story projects may be underway across the district.

You can find out more detail on #thebigwaterstory projects by visiting our website [www.chbdc.govt.nz](http://www.chbdc.govt.nz)



As part of Project Thrive, the importance of water to our community came through loud and clear!

Through the #thebigwaterstory we are bringing Project Thrive Alive.


## Key Projects Focus

Find out more below about some key projects currently happening in our community.




### Central Hawke's Bay Wastewater Improvements

June 2019 saw the culmination of a years' worth of work to prepare a response to the environment court in relation to a breach of resource consent conditions. The project now shifts to the next phase where the team will focus on continuing to improve the performance of the plants, developing a consenting strategy, progressing funding and financing work streams in preparation to take options to the community for a long term solution.

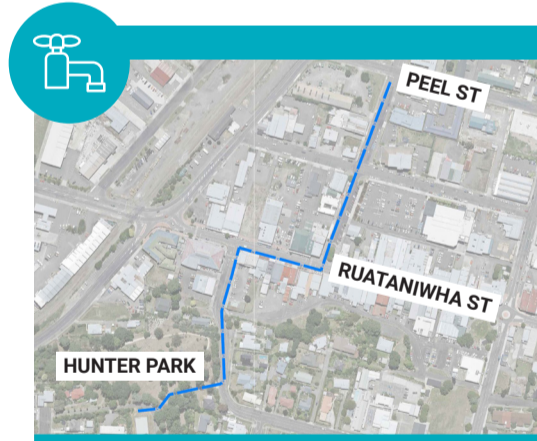

### Waipukurau Firefighting

From approximately Monday 29<sup>th</sup> July 2019 works are planned to commence on this project to improve firefighting capacity, shortfalls in supply and resilience of the Waipukurau water network. This project will see the first 2 of a 7 stage upgrade to the water network to better address security of supply, resolve areas of fire flow compliance, and allow for future connections within the urban boundary to service future growth.

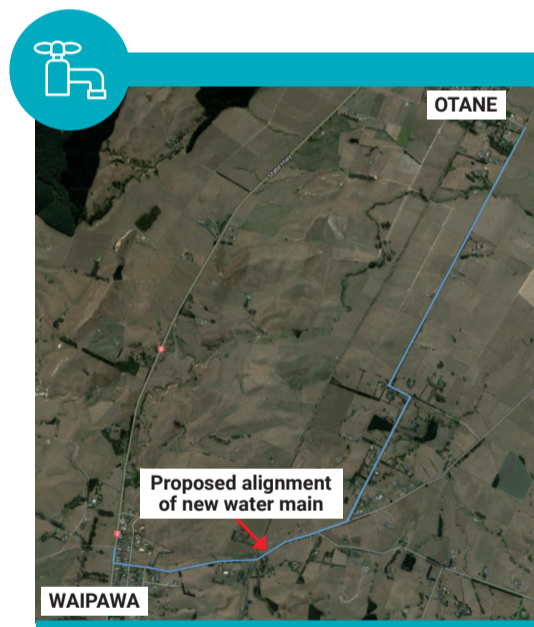

### Otane Alternate Water Supply

Works are expected to commence on-site the week of the 15<sup>th</sup> July 2019 on one of our largest projects within #thebigwaterstory through to expected completion in December 2019.

The construction will see a 180mm polyethylene (PE) pipeline laid from the existing Waipawa water supply on SH2, running along Racecourse Road, crossing the railway on Racecourse Road and running into and along White Road, finally connecting into new supply on the corner of Knorp and White Road. This exciting 5.2km new pipeline project will see significant resilience and security of water supply added to the Otane network.

## Individual Project Updates

WATER				
PROJECT	STATUS	TIMELINE	PROGRESS	BUDGET (TOTAL)
Otane Alternate Water Supply	Build	Start: Aug 2018 End: June 2020	20% ●○○○○	\$2.6m
Waipukurau Second Water Supply	Design	Start: Aug 2018 End: June 2021	10% ●○○○○	\$5.6m
Waipukurau SH2 Bore Upgrade	Contract Negotiations	Start: June 2018 End: Dec 2019	20% ●○○○○	\$850k
Waipukurau Firefighting and Shortfalls Improvements (Year 1-3)	Build	Start: Aug 2018 End: June 2021	20% ●○○○○	\$1.47m
Otane Land Development (Water and Wastewater)	Complete	Start: March 2018 End: Dec 2018	100% ●●●●●	\$355k
Waipukurau – Porritt Place Water Main Renewal	Complete	Start: Dec 2018 End: March 2019	100% ●●●●●	\$65k
Porangahau Water Treatment Plant Upgrade	Build	Start: Nov 2018 End: Oct 2019	30% ●●○○○	\$1.03m
Takapau Water Treatment Plant Upgrade	Build	Start: Nov 2018 End: Oct 2019	30% ●●○○○	\$680k
Waipukurau – Mackie/Mclean St Water Main Renewal	Build	Start: Nov 2018 End: Aug 2019	80% ●●●●○	\$391k

STORMWATER				
PROJECT	STATUS	TIMELINE	PROGRESS	BUDGET (TOTAL)
Waipukurau Stormwater Improvements – Service Lane Overflow	Design	Start: Aug 2018 End: Dec 2019	20% ●○○○○	\$132k
Waipukurau Stormwater Improvements – Savage/Churchill/Carpenter – Woburn/Wilder	Build	Start: Aug 2018 End: Dec 2019	20% ●○○○○	\$481k
Waipukurau Stormwater Helicoil Upgrades – Jellicoe to Tavistock	Build	Start: Aug 2018 End: Aug 2019	40% ●●○○○	\$219k
Waipukurau Stormwater Helicoil Upgrades – Francis Drake Street	Build	Start: Aug 2018 End: Aug 2019	70% ●●●●○	\$280k

WASTEWATER				
PROJECT	STATUS	TIMELINE	PROGRESS	BUDGET (TOTAL)
Waipawa Trunk Sewer Main Renewal	Engagement & Build	Start: Aug 2018 End: June 2020	20% ●○○○○	\$1.77m
CHB Wastewater Treatment Plants Project (Phase 1)	Engagement & Court Report	Start: June 2018 End: June 2019	90% ●●●●●	\$300k
CHB Wastewater Treatment Plants Project (Phase 2 – Design & Consent)	Investigation	Start: July 2019 End: Dec 2020	5% ○○○○○	\$1.8m
CHB Wastewater Treatment Plants Project (Phase 3 – Build)	Not Started	Start: Jan 2021 End: TBC	0% ○○○○○	TBC
Otane Wastewater Infiltration and Inflow Study	Build	Start: Jan 2019 End: June 2019	30% ●●○○○	\$80k
Otane Wastewater Treatment Plant Upgrade	Investigation	Start: April 2018 End: March 2021	40% ●●○○○	\$1.47m
Otane to Waipawa Wastewater Pipeline	Design	Start: June 2019 End: March 2021	5% ○○○○○	TBC
Takapau Wastewater Resource Consent Extension	Part 1 – Complete	Start: Aug 2018 End: June 2021	50% ●●○○○	\$100k
Takapau Wastewater Treatment Plant Upgrade	Not Started	Start: 2019 End: 2022	0% ○○○○○	\$831k
Porangahau/Te-Paerahi Wastewater Treatment Plant Upgrade	Not Started	Start: 2019 End: 2022	0% ○○○○○	\$1.85m
CHB Floating Wetlands Review	Investigations	Start: April 2019 End: TBC	5% ○○○○○	TBC
